




Consent Item

Notice of Completion for the Meniffee
Lakes Slurry Seal Phase 1 Project. PMP
19-03


A nighttime photograph of a cityscape with light trails from traffic on a highway. The city lights are visible in the background, and the light trails create a sense of motion and activity. The image is used as a background for the bottom half of the slide.

Jonathan G. Smith
Director of Public Works/City Engineer
December 4, 2019

Project Location

Communities:

- Country Gardens
- Mariposa
- Vista Estrella
- Saint Andrews

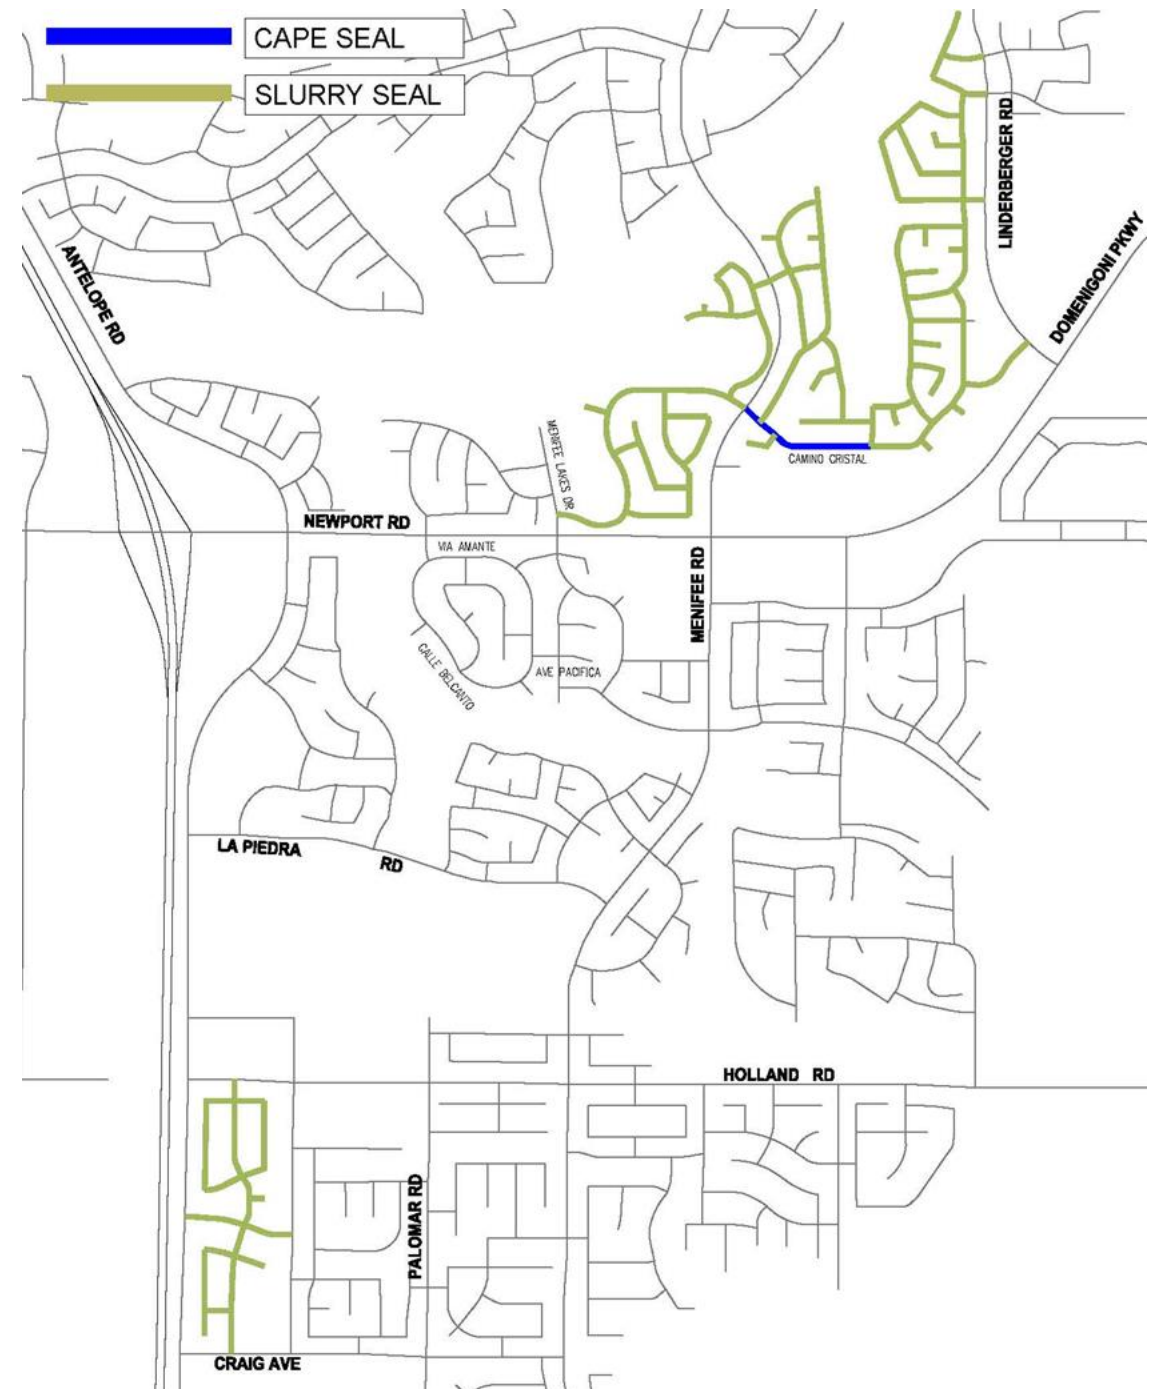

Discussion

Before



After





Discussion

Project Complete!

Improvements

- Re-surface existing streets with Type II Slurry Seal.
- New Stop Bars and Legends

Total Project Funding Breakdown

<i>Item</i>	<i>Budgeted</i>	<i>Actual</i>
Construction	\$407,586.15	\$380,568.04
Inspection	\$ 31,129.00	\$ 15,514.00
Labor Compliance	\$ 5,000.00	\$ 2,070.00
Total	\$443,715.15	\$398,152.04

Gas Tax **\$ 382,638.04**

Capital Projects **\$ 15,514.04**

TOTAL **\$ 398,152.04**

Project Team

Carlos Geronimo, Don Sharp, James Sloan

Contractor

American Asphalt South, inc.
