




Consent Item

Notice of Completion for the Quail Valley Community (West) Resurfacing Project.
PMP 19-02


Jonathan G. Smith
Director of Public Works/City Engineer
December 4, 2019

Project Location

- TYPE II SLURRY SEAL
- CAPE SEAL (CHIP AND SLURRY)

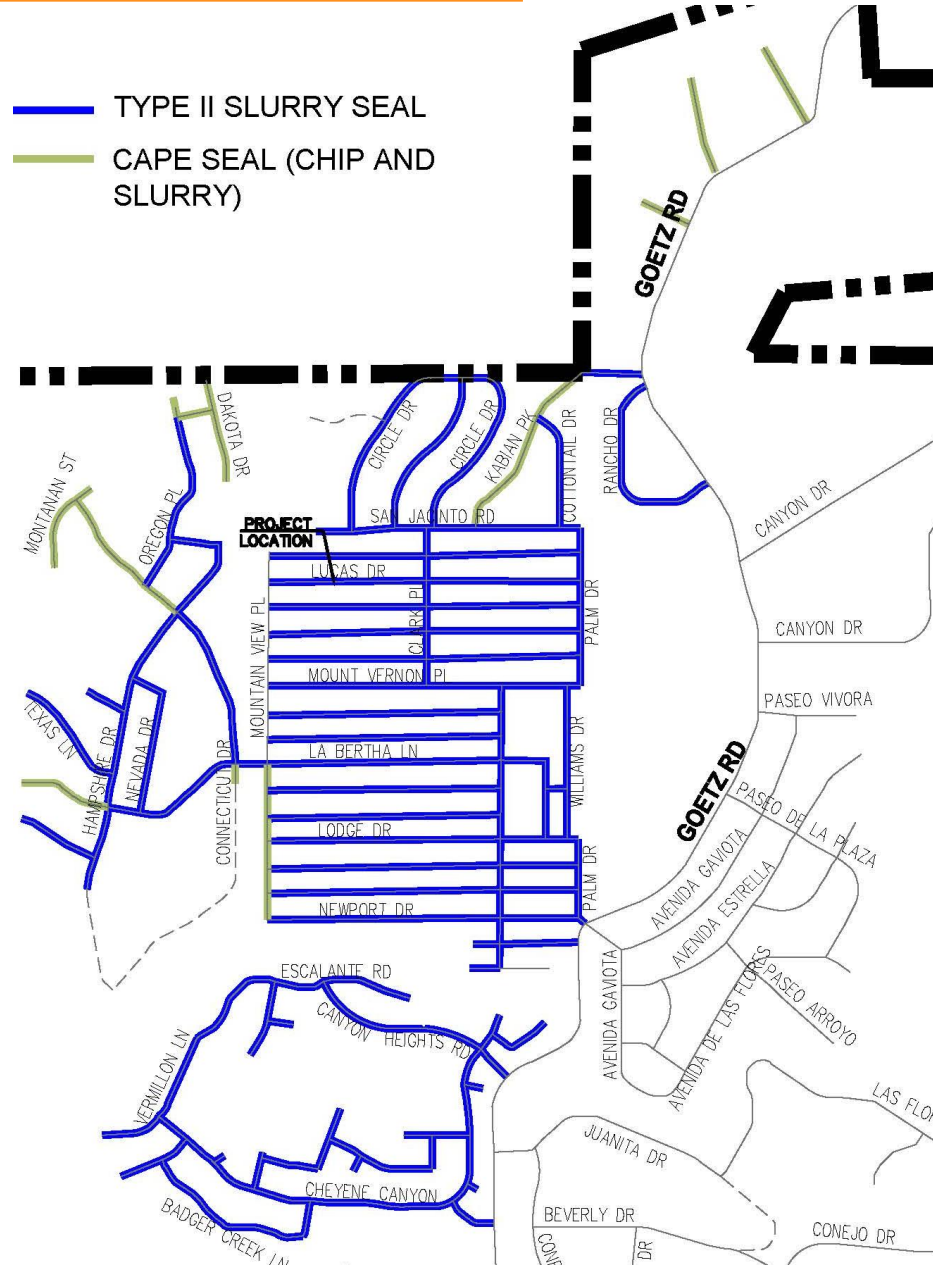

Discussion

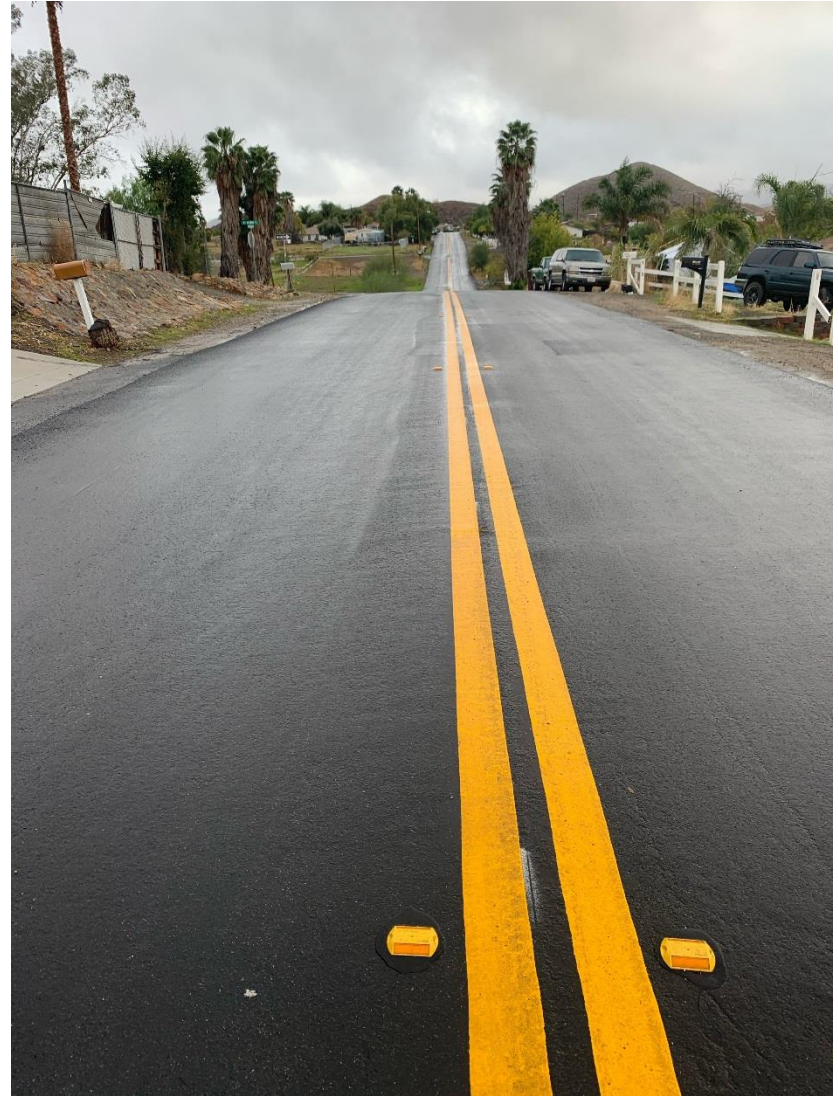

Discussion

Project Complete!

Improvements

- Re-surface existing streets with Cape Seal and Type II Slurry Seal.
- New Street Signs, Stop Bars and Legends

Total Project Funding Breakdown

<i>Item</i>	<i>Budgeted</i>	<i>Actual</i>
Construction	\$583,625.67	\$546,871.77
Inspection	\$ 40,000.00	\$ 16,238.00
Labor Compliance	\$ 12,000.00	\$ 2,238.00
Total	\$635,625.67	\$568,399.77

CSA 86 **\$ 568,399.77**

Project Team

Carlos Geronimo, Don Sharp, James Sloan

Contractor

American Asphalt South, inc.
